

ICL Pathway

**PATHWAY RELEASE POLICY**

Ref: PA/STR/003

Version: 3.0

**COMPANY IN CONFIDENCE**

Date: 28/06/99

---

**Document Title:** Pathway Release Policy

**Document Type:** Strategy Document

**Abstract:** This document defines the Pathway policy for the identification and planning of new Releases of Software and Data.

**Distribution:** Pathway Management Team

**Document Status:** APPROVED

**Document Predecessor:** 2.3

**Author:** Jim Morley, updated by Anne Cooper

## Contents List

<b>1. DOCUMENT CONTROL.....</b>	<b>3</b>
1.1 DOCUMENT HISTORY.....	3
1.2 CHANGES FORECAST.....	3
1.3 ABBREVIATIONS USED.....	4
<b>2. INTRODUCTION.....</b>	<b>4</b>
2.1 PURPOSE.....	4
2.2 DEFINITION OF RELEASE.....	4
2.3 IDENTIFICATION OF NEW BUSINESS OPPORTUNITIES.....	5
2.4 CHANGE CONTROL.....	6
2.5 CONTRACTUAL AND FUTURE RELEASES.....	6
<b>3. CLASSIFICATION OF RELEASES.....</b>	<b>7</b>
3.1 SOFTWARE RELEASES.....	7
3.1.1 <i>NEW PRODUCT RELEASES</i> .....	8
3.1.2 <i>INFRASTRUCTURE RELEASES</i> .....	9
3.2 REFERENCE DATA RELEASES.....	9
<b>4. DEFINITION OF RELEASE CONTENT.....</b>	<b>10</b>
4.1 RELEASE CONTROL & CONTENT.....	10
4.2 EMERGENCY PROCEDURES.....	11
<b>5. MAINTENANCE RELEASES.....</b>	<b>11</b>
<b>6. RELEASE SCHEDULE.....</b>	<b>12</b>
6.1 SOFTWARE RELEASES.....	12
6.2 REFERENCE DATA DISTRIBUTION.....	14

ICL Pathway

PATHWAY RELEASE POLICY

Ref: PA/STR/003

Version: 3.0

COMPANY IN CONFIDENCE

Date: 28/06/99

## 1. DOCUMENT CONTROL

### 1.1 DOCUMENT HISTORY

Version	Date	Reason
0.1	20/10/96	First Draft for Pathway internal use only
0.2	30/10/96	Second draft following application of Pathway comments.
0.3	30/10/96	Draft for issue to the PDA.
0.4	12/11/96	Updated following PDA comments through Michael Purchase.
0.5	17/11/96	Updated following PDA & Sponsor comments received through Michael Purchase.
0.6	18/11/96	Further comments applied from Pathway and PDA.
0.7	24/11/96	Further comments applied from PDA.
1.0	26/11/96	Further comments applied from POCL.
1.1	27/11/96	Further comments applied from PDA, BA and POCL
1.2	28/11/96	Incorporates revisions following review by Pathway, PDA, POCL and BA
1.3	1/5/98	Brought up to date to recognise differences between infrastructure and new product releases
2.0	29/03/99	Applied comments and approved ready for issue
2.1	21/05/99	Amended to reflect the current definition for Reference Data changes.
2.2	22/06/99	Amended to reflect the signed Heads of Agreement (24 <sup>th</sup> May 1999)
2.3	25/06/99	Amended to reflect comments from Pathway review
3.0	28/06/99	Further comments applied and approved ready for issue

### 1.2 CHANGES FORECAST

None.

ICL Pathway

**PATHWAY RELEASE POLICY**

Ref: PA/STR/003

Version: 3.0

**COMPANY IN CONFIDENCE**Date: 28/06/99

---

## 1.3 ABBREVIATIONS USED

The terms and abbreviations used in this document are those defined in Schedule A01 of the Agreement.

## 2. INTRODUCTION

### 2.1 PURPOSE

This document describes Pathway's policy for identifying and planning the development of new Releases of Software and data. Pathway aims to do this in a manner that is responsive to the business needs of POCL, and which also conforms to the provisions of the Agreement. Overall, it aims to:

- a) establish the principles associated with releases of Pathway Services in the context of the Agreement;
- a) establish the principles for regular and on-going Releases of the Pathway systems and Services; including infrastructure releases, new product releases and maintenance releases:
- a) establish the provisions to bring in changes to functionality and new POCL Clients more quickly and frequently through Reference Data provided by POCL and/or Pathway and to explain the main qualifiers for doing this;
- a) establish indicative timescales for the different types of Release in order to put these into context.

The Pathway Release Policy is a key element in the process of establishing business change, and provides a set of principles for the timely and efficient introduction of new or improved products and Services.

### 2.2 DEFINITION OF RELEASE

The Agreement defines a Release to be "a documented collection of Software and/or data provided by the CONTRACTOR to deliver a Service", while the Requirement 476 makes it clear that the definition also includes Reference Data. Throughout this document releases will be referred to as either Software Releases or Reference Data Releases. It is possible that both Software Releases and Reference Data Releases

require the co-ordinated implementation of other Infrastructure and Supporting Services and it will be seen that this requirement leads to further subdivisions of the definition of Releases later in the document.

## 2.3 IDENTIFICATION OF NEW BUSINESS OPPORTUNITIES

Releases are required to support changes of Service delivery in order to implement business change. This business change will cover a wide range of scale and complexity. For example:

- i. adjustment to POCL trading variables, such as the price of a first class stamp;
- i. changes to business rules, e.g. whether or not to print a receipt for Automated Payment Transactions;
- i. amending the format or information provided for existing transaction types;
- i. franchising an existing outlet, or creating a new outlet;
- i. implementing a new client for an existing service;
- i. introducing a new client transaction or new product ;
- i. re-engineering services within POCL's own operations.

The time, risk and cost of implementing such business changes will vary, depending upon the extent of:

- a) systems development;
- a) type of reference data changes;
- a) changes to Infrastructure;
- a) changes to support Services, such as Help Desk;
- a) changes to documentation;
- a) training requirements;
- a) changes to marketing collateral;
- a) network changes and telecommunications;
- a) clients process re-engineering;
- a) and so on.

ICL Pathway

**PATHWAY RELEASE POLICY**

Ref: PA/STR/003

Version: 3.0

**COMPANY IN CONFIDENCE**Date: 28/06/99

---

All these changes must be taken into account in the process of defining new business opportunities and setting priorities.

New business opportunities that require Releases will require a study to prepare and qualify the business case for POCL. It is anticipated that successful studies will result in an agreed Business Requirements Definition document, and that this would form the basis of a formal change request.

## 2.4 CHANGE CONTROL

A proposed change becomes contractually committed upon the presentation of a Change Control Note (CCN) by Pathway and its approval by POCL.

It is not required that Pathway should commit resources or expenditure to the development and implementation of a change until the CCN has been approved.

## 2.5 CONTRACTUAL AND FUTURE RELEASES

Release 1 was delivered in 3 phases: Release 1a (April 1997); Release 1b (May 1997); Release 1c (November 1997).

The CSR provides extended MIS functionality, introduces APS and EPOSS functionality, and passes information to POCL's interim TIP system for accounting and reconciliation purposes. CSR forms the basis for contractual acceptance, and will support the mounting of the Live Trial and so the launching of National Rollout.

The CSR+ will provide extended APS functionality, encompassing Smart Card functionality, and serves to sweep up the remaining outstanding contractual commitments from the original agreements and the introduction of LFS.

Further releases may be required on an ongoing basis. A number of new products are already envisaged to extend the range of business functionality available at the counter. There will, from time to time, be a need to refresh or extend the supporting infrastructure and the ongoing maintenance of the services will necessitate fault correction.

### 3. CLASSIFICATION OF RELEASES

Releases are classified as either Software Releases or Reference Data Releases.

Software Releases fall into 3 main categories: Infrastructure Releases, New Product Releases, and Maintenance Releases. In this section we deal with Infrastructure Releases and New Product Releases. Maintenance Releases are dealt with separately under section 5.

Similarly, Reference Data releases fall into a number of categories according to the impact and indicative timescales for implementation. It is emphasised that the classifications are not exhaustive and the timescales are intended to be indicative only. The classifications may also be reviewed in the light of experience.

#### 3.1 SOFTWARE RELEASES

Software Releases result from a number of different requirements to change or extend the Services.

This may be simply in order to maintain them in good working order, addressing faults, and improving service levels. Such Maintenance Releases are dealt with separately under section 5.

It may be that one or more additional areas of business functionality are required, perhaps introducing an entirely new service. This would give rise to a New Product Release.

The supporting infrastructure services will periodically need to be updated to take account of the infrastructure to support new products , releases or workload changes. So, depending on the nature of the changes required, different types of release are demanded. The impact of such changes measured in terms of the time, effort and risk and cost of implementing the changes will vary widely from one change to another , and these serve to characterise the different types of release.

Some changes will require extensive development effort and perhaps involve co-ordinated changes to Infrastructure and support Services, while others require only minor localised software development with little or no need for changes to the infrastructure or support services. Some can be implemented in a highly segregated manner, without disrupting too many of the existing components, whilst others may be highly invasive. As

a consequence some may require little in the way of re-integration effort, whilst others may require a great deal. All will require extensive and systematic testing of the areas concerned.

Between these extremes there is a continuum of the possible scale and complexity of implementation of changes, but according to their essential characteristics, all will fall into their respective categories of either New Product Release or Infrastructure Release.

Because of the development, integration and testing lead times involved with Infrastructure Releases, it is planned that a maximum of one a year could be implemented. Several New Product Releases may be planned each year, but in general releases should be spread out at least 3 months apart, and avoiding the busy Christmas period where POCL outlets are involved. Section 6 provides more information on timescales.

### 3.1.1 NEW PRODUCT RELEASES

The principal characteristics of the changes that form a New Product Release are as follows:

- a) Non-invasive changes, requiring little or no revision to the existing components of the services already operating
- a) May be implemented by the addition of discrete components, perhaps entire new services, highly segregated from the existing components, requiring little or no re-configuring of the existing services and their interfaces
- a) May be tested largely in isolation
- a) Imposes little or no re-integration of existing services
- a) Involves little or no migration from existing services
- a) Can be implemented with a backward compatible path, allowing gradual introduction across the network of POCL outlets, and as such permits the operation of a limited pilot
- a) Usually introduces significant new business functionality, and so requires significant levels of user training, which implies a requirement for a gradual training programme
- a) Several can be developed in parallel by virtue of the segregation, are typically of short duration, and can be implemented flexibly, either as separate releases or combined as one release

ICL Pathway

**PATHWAY RELEASE POLICY**

Ref: PA/STR/003

Version: 3.0

**COMPANY IN CONFIDENCE**Date: 28/06/99

---

**3.1.2 INFRASTRUCTURE RELEASES**

The principal characteristics of the changes that form an Infrastructure Release are as follows:

- a) Invasive changes, requiring significant revision to existing components of the services already operating
- a) Major infrastructure components refreshed, or significant re-configuring of the existing services and their interfaces
- a) Extensive service-wide regression testing required
- a) Imposes significant levels of re-integration of existing services
- a) May involve migration from existing service state
- a) May introduce major enhancements to existing business functionality

Cannot easily be developed in parallel because of the re-integration aspects, are typically of long duration, and must be implemented as planned and separate from other releases if possible. Because of the long lead-times such changes are generally best grouped together as one big release.

**3.2 REFERENCE DATA RELEASES**

POCL Reference data releases are governed by the Operational Business Change processes where the required business change has been defined and agreed in advance. Business changes that are implemented through Reference Data changes that do not fall into the definition of Operational Business Change, are governed by the normal Change Control process as described in this document.

The purpose of Operational Business Change (OBC) is to predefine common changes to the POCL business that occur often and require a short implementation cycle e.g. changing the price of a bus ticket. By pre-defining these changes the impacting cycle of the change is greatly reduced and the implementation actions and time scales can be defined in advance.

Operational Business Changes are initiated through the receipt of an OBC request form and Reference Data files, as defined in the process documents.

Reference Data Releases (under OBC) are broken down into more detailed change types according to the impact and indicative timescales

ICL Pathway

**PATHWAY RELEASE POLICY**

Ref: PA/STR/003

Version: 3.0

**COMPANY IN CONFIDENCE**

Date: 28/06/99

---

for implementation. The change types are documented in the "ICL Pathway/POCL Interface Agreement for Operation Business Change - Product" document. The interface agreement identifies specific types of business change in advance so that their characteristics (e.g. timescales, dependencies and responsibilities) can be understood by POCL when managing their business. These would be to support, for example, negotiation with clients and service management processes.

The broad categories of change type for Operational Business Change are:

- Outlet Advanced - requires additional activity from ICL Pathway e.g. relocating an outlet
- Outlet Basic - Class 1 reference data change only e.g. change of phone number
- Product Advanced - requires additional activity from ICL Pathway e.g. creation of new buttons on the counter menu
- Product Basic - Class 1 reference data change only e.g. change to the price of a bus ticket.

Class 1 Reference Data is reference data that has no additional impact on the Horzion system, although verification of the new data by POCL is required for High Risk changes.

## 4. DEFINITION OF RELEASE CONTENT

### 4.1 RELEASE CONTROL & CONTENT

The Requirement and Solution 476 refers to the testing, control and approval of Releases while the testing of Releases is described in Pathway's testing strategies and plans.

The content of a Release is determined through appropriate documentation baselined by one or more CCNs that shall be approved prior to a predetermined cut-off date for each Release. The purpose of this cut-off date is to ensure that the changes required in each Release are fully defined in time for the start of detailed design, development and testing. After the cut-off date changes may only be introduced under Change Control.

Requirement 476 requires POCL's approval (such approval not being unreasonably withheld) to the:

© 1999 ICL Pathway Ltd

ICL Pathway

**PATHWAY RELEASE POLICY**

Ref: PA/STR/003

Version: 3.0

**COMPANY IN CONFIDENCE**Date: 28/06/99

---

- contents of any release
- upgrade path for any release
- timing of the distribution of any release
- timing of the activation of any release

The definition of release content for any specific Release, and the development of any more detailed specifications, will need to take into account, amongst other things, the business priorities of the business changes in that Release and the alignment with associated Authority and Client systems. Processes for release content definition are to be developed to address such issues.

Processes will also be defined to address the co-ordinated development, trialing and introduction of Releases where these need to be aligned with POCL system releases e.g. TIP.

## 4.2 EMERGENCY PROCEDURES

Schedule A05 allows that if Pathway considers that any change is necessary in order for it to comply with its obligations under the Agreement and there is insufficient time to comply with the procedures then Pathway shall be entitled to proceed with such change, provided that it shall as soon as practicable provide POCL with a CCN for retrospective change. Such change shall be subject to the procedures described in Schedule A05, and if POCL, acting reasonably, do not agree to such change, such change shall be invalid and Pathway shall at its own expense promptly take all steps necessary to reverse and remove the effects of such change.

## 5. MAINTENANCE RELEASES

From time to time there will be a need for Releases of new Software and data in order to remove faults or to improve Service Levels without changing business functionality or business data. Such Releases are called Maintenance Releases.

Maintenance Releases will range in scope from very minor Releases which require little regression testing to major Releases that may require full Regression testing and the recalibration of SLA timings. The requirement for testing will be determined by reference to assessed technical and operational impacts for each overall Release and notified to POCL. Maintenance Releases shall be planned and implemented under

ICL Pathway

**PATHWAY RELEASE POLICY**

Ref: PA/STR/003

Version: 3.0

**COMPANY IN CONFIDENCE**Date: 28/06/99

---

Pathway's management control.

Minor maintenance releases that are designed solely to rectify faults reported to ICL Pathway through the incident and problem management process and that result in no associated changes to designed system functionality, process, procedure, training or documentation (bug fixes), will be applied to the system as soon as they have been authorised by ICL Pathway Customer Service Release Management. POCL Business Service Management will be notified that such releases have been applied at the regular Horizon Service Review Forum meetings and this shall be documented in the Horizon Service Review Book.

All other Maintenance Releases shall be subject to the Change Control procedure; and the Emergency Change procedure (Paragraph 4.2 above) shall be invoked only when immediate action is needed.

## **6. RELEASE SCHEDULE**

### **6.1 SOFTWARE RELEASES**

Pathway plans to implement approved changes in one or more Software Releases each year, disregarding those covered under Maintenance Releases (section 5) and Emergency Procedures (section 4).

In scheduling these releases a number of factors need to be considered.

Due to the long lead-times involved in Infrastructure Releases, largely stemming from the need to perform extensive re-integration, it is impractical to plan for more than one Infrastructure Release in a twelve month period.

Whatever the release type concerned, implementation periods need to be spread out to avoid conflict. The critical interval can be judged from the experience of other large service contracts. Experience dictates that they should be at least 3 months apart to achieve the optimum balance between the business imperative to introduce new functionality and the risk of adverse impact on Service Levels resulting from excessive rates of change.

Implementations involving the POCL outlets should be planned to avoid their busy Christmas period wherever possible.

New Product Releases, and some Infrastructure Releases will involve a phased implementation period, with user training activities and possibly

the running of a Pilot. These post go-live activities need to be scheduled in and taken into consideration regarding the scheduling of subsequent releases.

Under certain circumstances it may be advantageous to all parties to cluster a number of releases together into a single implementation period. This is particularly relevant to New Product Releases. The frequency of Releases will be reviewed in line with experience gained during live operation. The current view is that between 2 and 3 releases are likely each year, comprising one Infrastructure release and one or two New Product Releases. (These may be combined releases, depending on the size and the complexity of each.)

The relationship between the release definition activities and the ultimate implementation of the release is illustrated below:

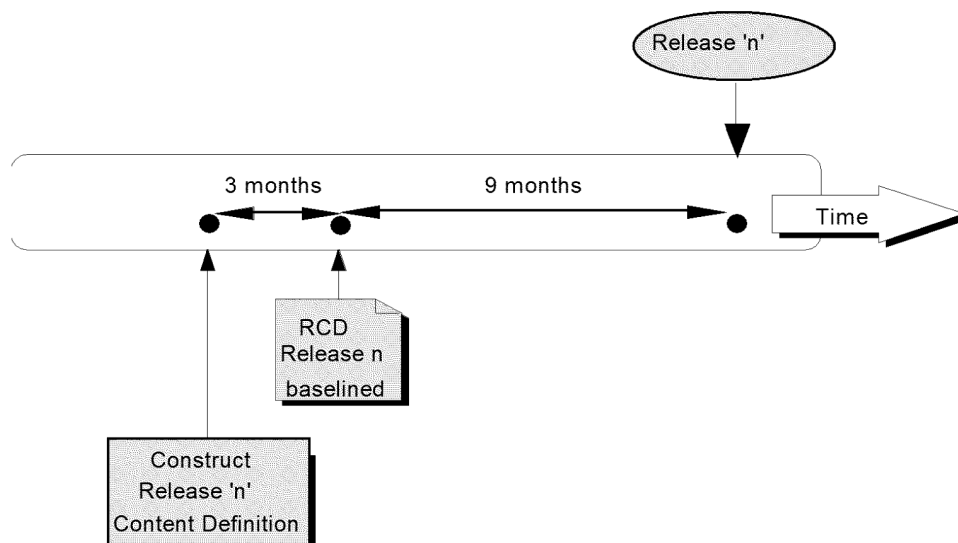


Fig 6.1 - Release Planning

Changes which have been approved within the Validity Period of the associated CCN will be included within the Release Contents Definition for the Release stated. Three months are allowed for the approval of each Release Contents Definition which is then baselined while the Release is implemented. Thus in steady state, there will be at any time, one live Release (Release “n”) and two new Releases ( n+1 and n+2) at different stages of design and implementation.

The table below illustrates a possible timetable for, say, a combined

release comprising maybe 2 New Product Releases delivered in the Autumn, then avoiding the Christmas period, and then an Infrastructure Release encompassing some functional enhancements, delivered in the following Spring.

Release Contents Baseline	Design	Development	Test & Integration	Implement	Release
1 January	1 Jan - 28 Feb	1 Feb - 31 May	1 Apr - 30 Sep	1 Sep - 30 Nov	1 October
1 July	1 July - 31 July	1 Aug - 31 Oct	1 Nov - 28 Feb	1 Mar - 31 May	1 April

Fig 6.2 - Release Timetable

In constructing the illustrative timetable shown above, Pathway has assumed that the Test & Integration period will encompass a period of one month (not exclusive) within which POCL undertake any Joint testing of the Release that may be required. It is anticipated that the testing and acceptance processes after the initial releases will be rationalised by mutual agreement.

For the avoidance of doubt, if an element of the Services under test fails its testing criteria and it is decided by POCL and Pathway to withdraw it in order to maintain Release timescales, then that failed element will be included in the next Release unless otherwise agreed.

## 6.2 REFERENCE DATA DISTRIBUTION

Indicative timescales for the implementation of the different classes of Reference Data Release are provided in document "ICL Pathway/POCL Interface Agreement for Operation Business Change - Product".
